

RESOLUTION NO. 23-135


A RESOLUTION OF THE CITY OF PANAMA CITY BEACH, FLORIDA, APPROVING A CHANGE ORDER TO THE CITY'S AGREEMENT WITH CWR CONTRACTING, INC., FOR THE FRONT BEACH ROAD SEGMENT 3 PROJECT, TO ADD \$112,142.80 AND FOURTEEN DAYS FOR PERFORMANCE OF THE WORK.

BE IT RESOLVED that the appropriate officers of the City are authorized to execute and deliver on behalf of the City that certain Change Order No. 6 to the Agreement between the City and CWR Contracting, Inc., for the Front Beach Road Segment 3 Project, to add One Hundred Twelve Thousand, One Hundred Forty-Two Dollars and Eighty Cents (\$112,142.80) and fourteen (14) days for performance of work related to resolving conflicts between AT&T utility facilities and the proposed stabilization of the new roadway subgrade, in substantially the form **attached** and presented to the Council today, with such changes, insertions or omissions as may be approved by the City Manager and whose execution shall be conclusive evidence of such approval.

THIS RESOLUTION shall be effective immediately upon passage.

PASSED in regular session this 9th day of March, 2023.

CITY OF PANAMA CITY BEACH

By: 
Mark Sheldon, Mayor

ATTEST:


Lynne Fasone, City Clerk

CHANGE ORDER

No. 6

PROJECT	Front Beach Road CRA Segment 3		
DATE OF ISSUANCE	March 9, 2023	EFFECTIVE DATE	March 9, 2023
OWNER	City of Panama City Beach, Florida		
OWNER's Contract No	2018-01		
CONTRACTOR	CWR Contracting, Inc.	ENGINEER	Dewberry Engineers

You are directed to make the following changes in the Contract Documents

Description: 1) Create Contract Pay Item 285-704 - Optional Base Group 4

Quantity = 4840 SY, Unit Price = \$23.17 per SY

This work is authorized to allow Contractor to proceed despite failure of AT&T to timely relocate its existing telephone facilities out of conflict with mixed-in-place roadway subgrade specified in contract plans. Reimbursement for cost will be pursued with AT&T by City of Panama City Beach. All claims against City for AT&T conflicts in subgrade areas from Cabana Cay Blvd. to San Vincente Street are herein released by Contractor in consideration of this compensation and time extension.

Reason for Change Order:

Change in materials and method of subgrade stabilization is required to avoid damaging existing AT&T facilities that are located within the proposed mixed-in-place subgrade. Use of the original method of subgrade stabilization would result in damage to shallow AT&T facilities and cause interruption of telephone service.

Attachments: Exhibit "A" - 3 pages - Proposed subgrade areas to be modified

	CHANGE IN CONTRACT TIMES:	
Original Contract Price	Original Contract Time:	560
\$28,003,403.41	Substantial Completion:	November 24, 2022
	Final Completion	December 24, 2022
		days or dates
Net Changes from previous Change Orders	Net changes from previous Change Orders	
\$1,788,302.48	447	
	days	
Contract Price prior to this Change Order	Contract Time prior to this Change Order	
\$29,791,705.89	Substantial Completion:	February 14, 2024
	Final Completion	March 15, 2024
		days or dates
Net <u>Increase</u> of this Change Order	Net <u>Increase</u> of this Change Order	
\$112,142.80	14	
	days	
Contract Price with all approved Change Orders	Contract Times with all approved Change Orders	
\$29,903,848.69	Substantial Completion:	February 28, 2024
	Final Completion	March 29, 2024
		days or dates

RECOMMENDED:

By: _____
Engineer (Authorized Signature)

Date: _____

APPROVED

By: _____
(Authorized Signature)


Date: _____

ACCEPTED

By: _____
Contractor (Authorized Signature)

Date: _____

Change Order #6
Exhibit "A"

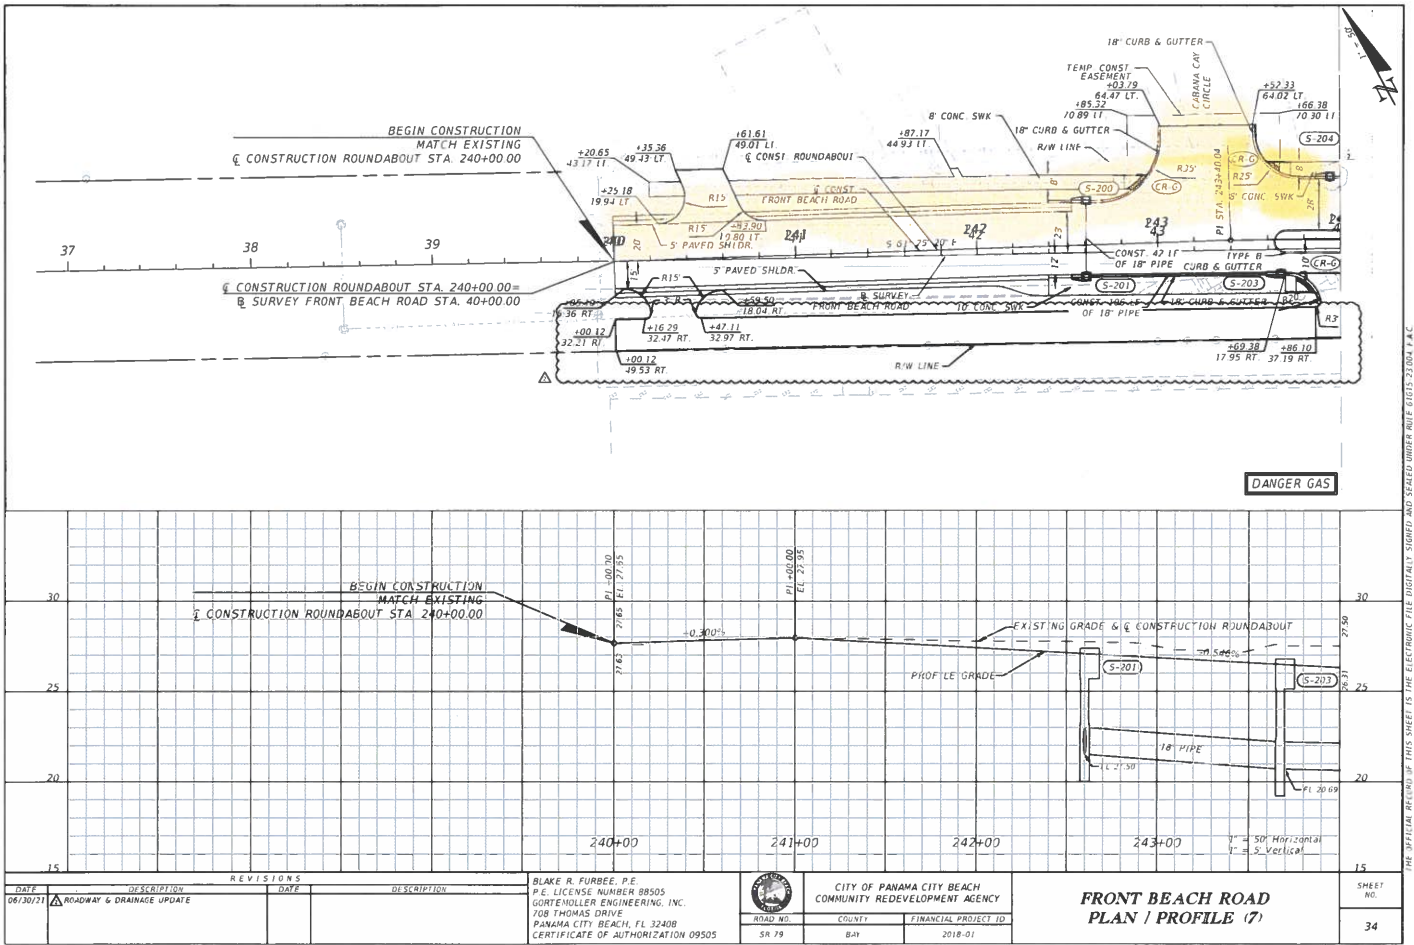

Change Order #6
Exhibit "A"

